

WARNING

THIS PLAN MAY NOT BE ACCURATE

CENTRAL HIGHLANDS WATER ACCEPTS
NO RESPONSIBILITY FOR INACCURACIES IN
THE INFORMATION CONTAINED ON THIS PLAN

BALLARAT SEWERAGE AUTHORITY.

Sewerage Area No. 22 MASTER PLAN

Detail Plan No. 10

Drainage Plan No. 1622

AMENDED PLAN OF DRAINAGE [M.P.1622]

FOR

1623
5263 5211

N^o 103. Miss M McTighe, D.S.O.

N^o 105. Mr J.A.C. Thomas III Lyons St. Sth.

N^o 105^A Mr M.H. Bade (Mr W.E. Traits, 9 Ajax St. Agent) N^o 105^A Mr F. Taylor
9 Ascot St. Sth.

MUNICIPALITY: CITY OF BALLARAT.

REFERENCE

B.T. Boundary Trap
D.T. Disconnecter Trap
G.T. Gully Trap
G.D.T. Gully Disconnecter Trap
G.I.T. Grease Interceptor Trap
G.S.T. Gully Silt Trap
S.V. Stop Valve

S.I.V. Sluice Valve
S.T. Silt Trap
C.I.P. Cast Iron Pipe
G.W.I.P. Galv. Wrought Iron Pipe
S.P.D. Stoneware Pipe Drain
I.C. Inspection Chamber
I.O. Inspection Opening
R.V. Relief Vent

E.V. Educt Vent
I.V. Induct Vent
S.I.V.P. Soil Induct Vent Pipe
S.V.P. Soil Vent Pipe
T.I.T. Triple Interceptor Trap

(See By-Law No. 2, B.S.A., Specification, and General Conditions of Contract, 1622 - 15/- Paid)

APP. 5211 PLAN FEE 15/- PAID

APP. 5263 PLAN FEE 15/-

APP. 5263 AMENDMENT FEE 3/6

AMENDED FURTHER ADDITIONAL WORK FEE APP. 1623 - 8/6

Scale 40 feet to 1 inch.

PLAN FEE

APP. 1623 - 15/- Paid

NOTE: - These Properties are to be drained by a combined operation.


ADDITIONAL WORK FEE APP. 1623 7/6

AMENDMENT FEE APP. 1623 - 5/-

FEE FOR COPY OF PLAN APP. 1623 7/6 1/6

PD. AMENDMENT FEE APP. 1622 - 2/6 Paid

FUR. ADD. WORK FEE APP. 1623 1/6

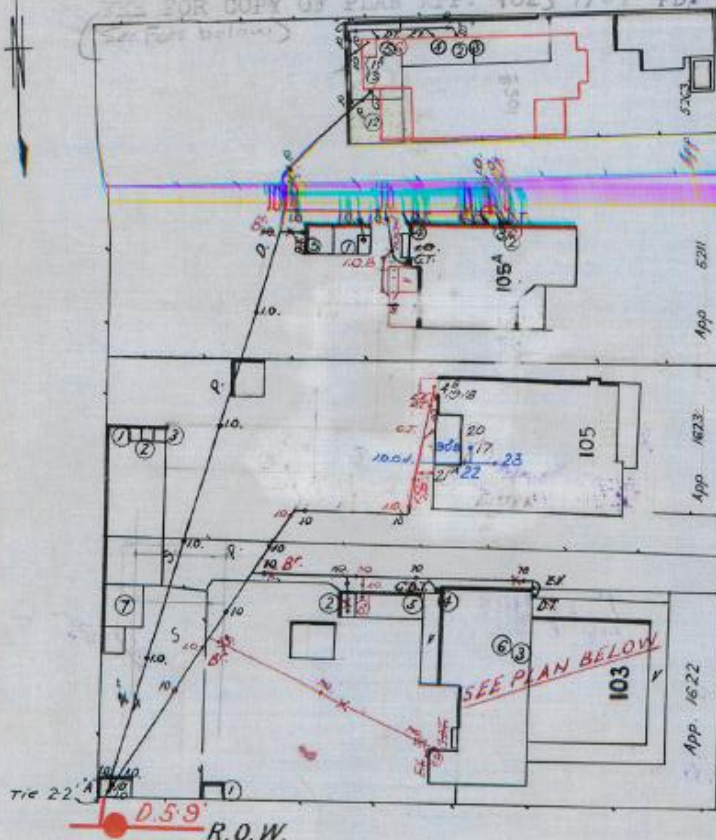

FITTINGS.

103 LYONS STREET SOUTH

1. Closet to be abolished.
2. Closet external proposed.

4. Sink.
5. Wash Troughs - regulation pipe to be provided.
6. Lavatory Basin to be replaced.
7. Stable to be abolished.

105 LYONS STREET SOUTH

- 1, 2, 3. Closets to be abolished.
4. Closet external proposed.
5. Bath to be abolished.
6. Sink to be abolished.
7. Sink to be moved to 8.
9. Wash Troughs.
10. Lavatory Basin proposed.
11. Lavatory Basin to be replaced.
12. Stable to be paved with bricks on edge on 3rd ear or ashes grouted full depth with cement mortar and graded to 8 ft.
13. Stable to be abolished.
14. Manure Bin to be repaired and cover provided. (First Floor)

15. Bath to be replaced. No Lead safe required.
 16. Lavatory Basin to be replaced. No Lead Safe required.
- S.P.D. near trees to be surrounded with concrete or trees to be grubbed out.

G.D.T. & G.T. to be built up with radial bricks or cement concrete rendered internally and on top to a smooth surface, and 15 in. internal diameter. Tap and apron to be provided.

AMENDED FITTINGS.

103 LYONS STREET SOUTH.

Arthur Lister
Engineer-in-Chief

DATE 29. MAR 1928

o. Lavatory Basin to be abolished.

Arthur Larsson
Engineer-in-Chief
DATE 8 AUG 1928

AMENDED FITTINGS.

105 LYONS STREET SOUTH.

12. Stable to be abolished.

Arthur Larsson
Engineer-in-Chief
DATE 5 MAY 1928

4.4

4.4 7A 7A 7A Examin'd

Date 28 MAR 1928
7 AUG 1928

105 LYONS STREET SOUTH.

ADDITIONAL WORK
(Shown in Curbing).

- 4. Closet external to be abolished.
- 8. Sink to be abolished.
- 9. Wash Troughs to be abolished.
- 10, 11. Lavatory Basins to be abolished. (First Floor)
- 15. Bath to be abolished.
- 16. Lavatory Basin to be abolished.
- I.V.'s to be abolished.
- Drain and Trap to be sealed as directed.

AMENDED FURTHER ADDITIONAL WORK.

105 LYONS STREET SOUTH.

4A. Closet external to be moved to 4B.

Arthur Larsson
Engineer-in-Chief
DATE 14 JUNE 1930

FITTINGS.

105A, LYONS STREET SOUTH.

- 1. Closet external to be abolished.
- 2. Bath to be abolished.
- 3. Basin to be abolished.
- 4. Sink to be abolished.
- 5. Troughs to be abolished.
- S.P.D. under building to be taken up.
- S.P.D. from "A" at 103 Lyons Street to "B" at 105 Lyons Street to be laid at a grade of 1 in 66 without J.U.

Arthur Larsson
Engineer-in-Chief
DATE

FITTINGS.

105B, LYONS STREET SOUTH.

- 1. Closet external proposed (door to face East).
- 2. Bath proposed.
- 3. Basin proposed.
- 4. Sink proposed.
- 5. Troughs proposed.

S.P.D. from "B" to "C" to be laid at 1 in 66.

G.T. to be built up with radial bricks or cement concrete rendered internally and on top to a smooth surface, and 15 in. internal diameter. Tap and apron to be provided.

Arthur Larsson
Engineer-in-Chief
DATE

3 SEP 1931
5 JUL 1946

(Fees Cont. from above)

ADDITIONAL WORK FEE APP. 1622	-	12/6
ADDITIONAL WORK FEE APP. 5211	-	15/-
FUR. ADD. WORK FEE APP. 1623	15/-	} 27/6 PAID
NO. 2 COPY OF PLAN APP. 1623	12/8	
M. FUR. ADD. WORK FEE APP. 1623	10/-	
ADD. WORK FEE APP. 5263	\$1.00	
FOR COPY OF PLAN APP. 5263	1.25	\$2.25

No. 105³

AMENDED FITTINGS.

1. Closet external to be abolished.

Arthur Larsson
Engineer-in-Chief
DATE 4 SEP 1931

ADDITIONAL WORK.
103 LYONS STREET SOUTH.
(Shown in Carmine)

- 8. Closet external proposed.
- 9. Sink proposed.
S.P.D. near trees to be surrounded with concrete or trees grubbed out.

S. J. Sullivan
OFFICER IN CHARGE
OF HOUSE CONNECTIONS
DATE: 5 JUL 1946

ADDITIONAL WORK.
(Shown in Carmine)

105A LYONS STREET SOUTH.

- 6. Closet internal proposed. Permanent and efficient light and ventilation to be provided. No storage tank to be provided. (Request 21/8/61).
S.P.D. not in use to be abolished.

S. J. Sullivan
OFFICER IN CHARGE
OF HOUSE CONNECTIONS
DATE: 6 SEP 1961

Ed
15 DEC 1967

FURTHER ADDITIONAL WORK.
(Shown in Carmine)

105 LYONS STREET SOUTH.

- 21. Closet internal proposed. Permanent and efficient light and ventilation to be provided. No storage tank to be provided. (Request 22/9/61).
S.P.D. under building to be surrounded with concrete.

S. J. Sullivan
OFFICER IN CHARGE
OF HOUSE CONNECTIONS
DATE: 8 OCT 1961

FURTHER ADDITIONAL WORK.
105A LYONS ST STH.

- 5. Troughs to be abolished.
- 7. Trough proposed.
- 8. Washing Machine proposed.
S.P.D. not in use to be abolished and O.B. sealed as directed.

Barrows
OFFICER IN CHARGE
DATE: 12. 6. 84

AMENDED FURTHER ADDITIONAL WORK.
(Shown in Carmine)

105 LYONS STREET SOUTH.

- 21A. Closet internal proposed. Permanent and efficient light and ventilation to be provided. No storage tank to be provided. (Request 22/9/61). Pan to be vented off heel of C.I. I.O. bend.

S. J. Sullivan
OFFICER IN CHARGE
OF HOUSE CONNECTIONS
DATE: 1 NOV 1961

FURTHER ADDITIONAL WORK

105 Lyons St Sth

- 7 Bath to be abolished
- 0 Basin to be renewed
- 2 Closet proposed
- 3 Shower proposed

J. P. Baine
OFFICER IN CHARGE
DATE: 18. 6. 92

ADDITIONAL WORK.

105B LYONS STREET SOUTH.

- 1A. Closet to be made internal. Permanent and efficient light and ventilation to be provided. No storage tank to be provided. (Request 12/12/67). Pan to be vented as directed.
- 3. Basin to be renewed.
- 4. Sink to be renewed.
- 5. Troughs to be renewed.
- 6. Washing Machine proposed.

D. J. Nicholson
OFFICER IN CHARGE
OF HOUSE CONNECTIONS
DATE: 19 DEC 1967

FURTHER ADDITIONAL WORK
No. 103 LYONS STREET SOUTH

- All existing fittings to be abolished.
- 1. Closet internal proposed
- 2. Closet internal proposed
- 3. Bath proposed
- 4. Basin proposed
- 5. Basin proposed
- 6. Shower proposed
- 7. Shower proposed
- 8. Sink proposed
- 9. Trough proposed
- 10. Washing Machine proposed
- S.P.D. not in use to be abolished and O.B.'s 2 No. sealed as directed.

New 100mm point of connection to be constructed in sewer main by the Authority at owner's expense after necessary excavation by owner. Authority requires 48 hours notice before excavation will be inspected.

Barrows
DATE: 2. 8. 82.



WARNING
THIS PLAN MAY NOT BE ACCURATE
CENTRAL HIGHLANDS WATER ACCEPTS
NO RESPONSIBILITY FOR INACCURACIES IN
THE INFORMATION CONTAINED ON THIS PLAN

Lyons Street South
